

Project details

- Customer: Lilama 18 - Torishima
- December 2010: erection & commissioning of Vivablast Workshop for Vung Ang 1 TPP internal & external lining of main cooling water piping Project
- Location: Vung Ang Industrial Zone, Ha Tinh Province, Vietnam
- Erection and commissioning duration: 20 days
- Direct Manpower: 30

Heavy-duty equipments mobilized:

- 16 containers 40ft mobilized from HCMC
- 1 bus transportation 45 seats
- 1 crane 25 tons
- 2 cherry picker ATJ 180
- 1 forklift



- Concrete slab casting & all civil works executed by Lilama 18 prior Vivablast equipments, materials & manpower mobilization



- Mobilization from HCMC of 16 40ft containers at site before beginning the installation of the blasting chamber on the finished area of the concrete platform



■ Beginning the installation of the blasting chamber on the finished area of the concrete platform



■ Cabin floor preparation



■ Cabin assembling



■ Floor blasting room assembling



■ Machinery installation



■ Duct distribution installation



■ Air filter erection



■ Blasting room wall installation



■ Preparation for light system installation.



■ Blasting room filter machinery installation



■ Erection of roof cladding of paint shop & blasting shop. Mani access.




■ Workshop erection



■ Rail assembling inside blasting room



■ Blasting room electrical and lighting system completed

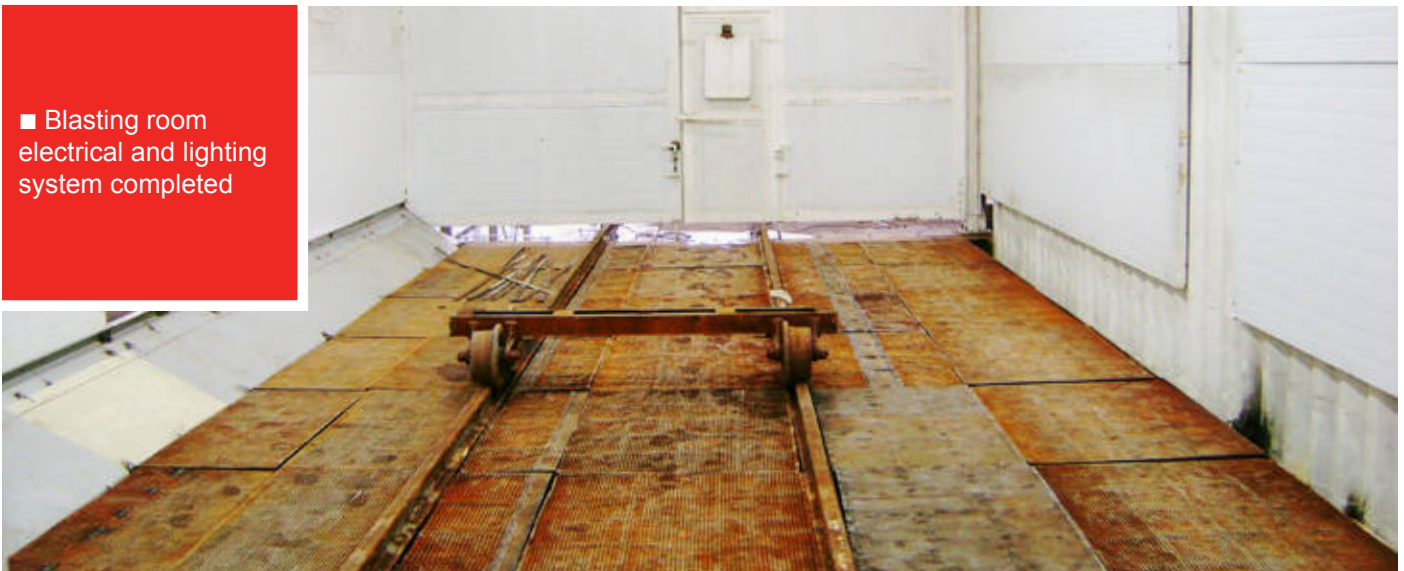

■ Rail installation at exit door (100m total for painting line)



■ Installation and commissioning of air compressors, electrical system, other blasting & painting equipments



■ Commissioning of blasting chamber and other tests



■ The Vung Ang Workshop erected and commissioned in 20 days

