

■ **Project details**

- Customer: DP Consulting
- Location: VIN MEDICARE HOSPITAL 460 Minh Khai Street, Hai Ba Trung District, Hanoi, Vietnam
- Scope of works: spray 200 mm of Sprefix glass wool spray on insulation on the ceiling and walls of the Genset Room and cover with glass fiber reinforced aluminum foil.
- Mobilization and erection of 4 tons of british standard scaffolding materials for safe scaffold platform
- Start works on 11 December 2011 (on-going) – target works completion on 22 December 2011

■ **STEP 1**

- Erecting a safe scaffolding platform to access the ceiling




■ **STEP 2**

- Spraying first insulation layer of 100mm on the ceiling



STEP 3

■ The first insulation layer is sprayed on one third of the ceiling area. The spraying works continue on the remaining ceiling area

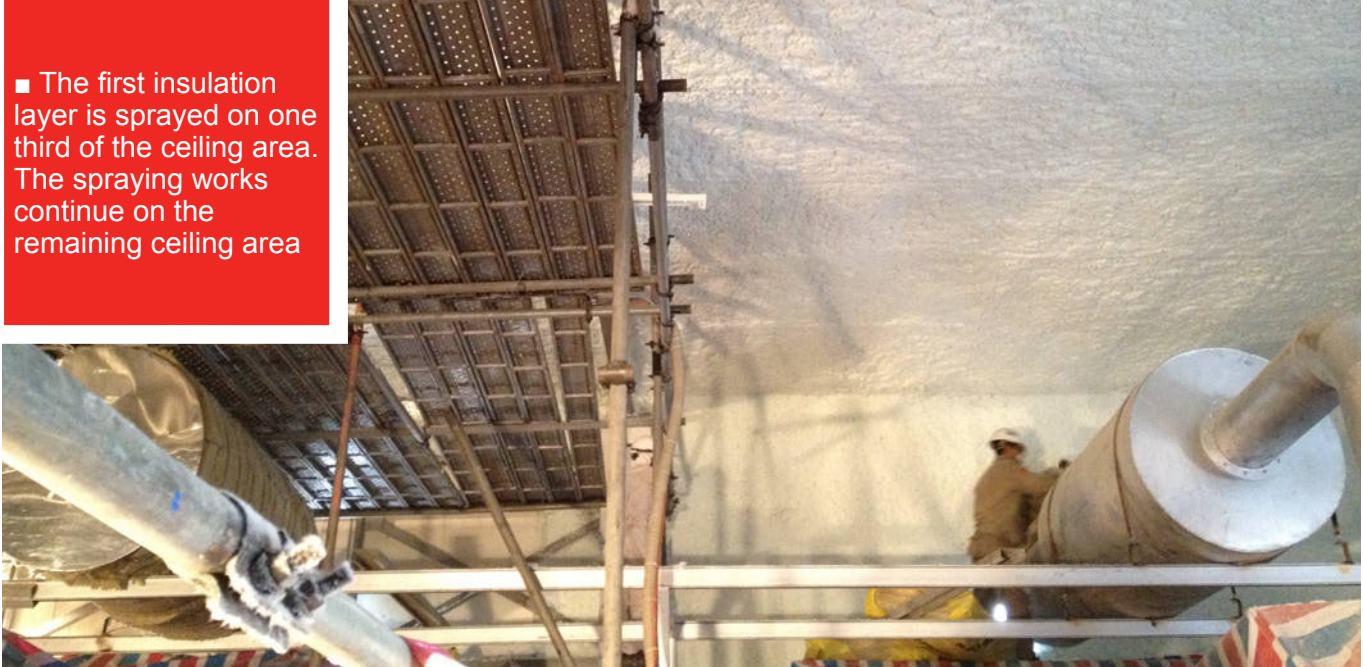

STEP 4

■ The sprefix machine is operated full time by Vivablast certified Technicians



■ **STEP 5**

■ 200 mm of insulation is already sprayed on 35% of the Genset Room walls



■ **STEP 6**

■ Swedish OVACON Technical Manager & VIVABLAST Project Manager check carefully the quality of the insulation with DP Consulting Site Manager

